SOFTWARE ENGINEERING LAB 2

Jira Agile Project Deliverables

Remote Team Time Tracker

Submission component	Included evidence
Epics and user stories	Epic register, story register, backlog and timeline screenshots
Gantt / project plan	Jira timeline with sprint and epic scheduling
To Do / In Progress / Done	Active sprint board, backlog status and summary metrics
Retrospective	What went well, improvements, action items and lessons learned

Prepared from the supplied Jira screenshots captured on 31 August 2026. Entries obscured or not visible in the screenshots are explicitly identified rather than inferred.

1. Deliverables checklist

The evidence package follows the four items shown on the laboratory deliverables board.

#	Required deliverable	Evidence in this PDF	Status
1	Screenshots of epics and user stories created in Jira	Epic and story tables; backlog and timeline screenshots	Included
2	Project timeline / Gantt-style plan	Jira Timeline showing sprint and scheduled epic bars	Included
3	To Do, In Progress and Done workflow	Active Sprint board, backlog states and summary charts	Included
4	Retrospective: what happened, summary and lessons	Structured retrospective with actions and learning	Included

Project snapshot

Project	Board	Total work items	Created	Completed shown	Due soon
Remote Team Time Tracker	CK board	20	20	9	0

The final summary screenshot reports 20 total work items, 20 created, 9 completed and 11 in To Do. Earlier screenshots show progress changing from 5 completed / 15 To Do to 9 completed / 11 To Do.

2. Epic register

The Jira timeline displays six epic records. CK-5 and CK-6 use the same visible label in the supplied screenshot.

Key	Epic	Purpose / scope	Screenshot evidence
CK-1	Jira Task Synchronization	Bring assigned Jira work into the time-tracking workflow.	Timeline; backlog
CK-2	Time Entry Management	Create, edit and validate draft time entries.	Timeline; backlog
CK-3	Timesheet Submission and Approval	Submit, lock, review, approve or reject timesheets.	Timeline; backlog
CK-4	Project Budget Monitoring	Expose budget burn and threshold alerts.	Timeline; backlog
CK-5	Performance, Security, and Auditability	Non-functional controls for performance, scoped access and auditability.	Timeline
CK-6	Performance, Security, and Auditability	Second Jira epic record with the same visible title.	Timeline

Epic scheduling summary

Epic	Visible schedule state	Interpretation
CK-1	Short purple bar in early September	Scheduled in the displayed timeline
CK-2	Short amber bar in early September	Scheduled in the displayed timeline
CK-3	Longer coral bar in September	Scheduled for a longer window
CK-4 to CK-6	No visible bar in the captured viewport	Dates are not demonstrated by the supplied screenshot

3. User story register

The table records every story title that is legible in the supplied evidence. CK-12 and CK-13 are not legible in any supplied screenshot, so they are retained as evidence gaps instead of being guessed.

Key	User story / work item	Epic	Points	Observed status
CK-7	View Assigned Jira Tasks	Jira Task Synchronization	3	Done
CK-8	Synchronize Jira Tasks	Jira Task Synchronization	5	Done
CK-9	Create Draft Time Entry	Time Entry Management	5	Done
CK-10	Edit or Delete Draft Entry	Time Entry Management	3	Done
CK-11	Enforce Daily Hour Limit	Time Entry Management	3	Done
CK-12	Not visible in supplied screenshots	Not verifiable	-	Evidence gap
CK-13	Not visible in supplied screenshots	Not verifiable	-	Evidence gap
CK-14	Lock Submitted Timesheet	Timesheet Submission and Approval	5	Done
CK-15	Review and Approve Timesheet	Timesheet Submission and Approval	3	Done
CK-16	Reject Timesheet with Feedback	Timesheet Submission and Approval	8	Done
CK-17	View Budget Burn Dashboard	Project Budget Monitoring	5	To Do
CK-18	Receive Budget Threshold Alerts	Project Budget Monitoring	8	To Do
CK-19	Enforce Secure Scoped Access and Audit	Performance, Security, and Auditability	8	To Do
CK-20	Meet Peak Performance Target	Performance, Security, and Auditability	5	To Do

4. Sprint and workflow summary

Sprint	Visible dates / state	Included work	Outcome
Sprint 1 - Time Capture	31 Aug - 7 Sep	CK-7 to CK-11; 19 story points	Five visible items completed
Sprint 2 - Time Capture 2	Completion dialog shown	Four completed work items; 21 points visible on backlog	Ready to complete

Workflow state	Evidence	Interpretation
To Do	11 items in final summary; CK-17 to CK-20 visibly To Do	Remaining backlog is queued
In Progress	No items in the final summary snapshot	No visible work-in-progress at capture time
Done	9 items in final summary; Sprint 1 stories visibly Done	Two batches of work were completed

Burndown and reporting observations

The Sprint 1 burndown guideline begins at 19 story points and trends to zero by 7 September. The Sprint 2 chart begins at 16 story points. Jira reporting also shows a work-item creation trend and an average issue cycle-time point of approximately 156 seconds for the displayed completion date. These screenshots document configured reporting views; they should not be treated as a complete longitudinal performance dataset.

5. Sprint retrospective

Retrospective based on the supplied Jira evidence.


Area	Summary	Evidence / implication
What went well	The team created a coherent hierarchy of epics and stories, estimated visible stories, organized work into sprints, and moved the first time-capture batch to Done.	Five Sprint 1 items are Done; the later summary reports nine completed items.
What happened	The first sprint focused on Jira synchronization and draft time entry. The second completed the core timesheet approval flow. Budget and non-functional stories remained in the backlog.	Backlog, sprint board, summary and completion dialog show the sequence.
What could improve	Two story records are obscured in the supplied evidence, duplicate-looking epic names reduce traceability, and assignees appear unset in the screenshots.	CK-12 and CK-13 cannot be verified; CK-5 and CK-6 share a visible title; user icons show no named assignee.
Process improvement	Capture a full expanded backlog, use unique epic names, assign owners, add acceptance criteria, and take screenshots only after statuses and dates are finalized.	Improves auditability and removes ambiguity in future submissions.
Planning improvement	Keep sprint dates and estimates current and review the burndown throughout the sprint rather than only at completion.	Creates useful trend data and earlier warning of slippage.

Action items


Priority	Action	Expected benefit
High	Rename or clarify CK-5 and CK-6; capture CK-12 and CK-13 in an expanded backlog view.	Complete, unambiguous requirements traceability
High	Assign an owner and acceptance criteria to every story before sprint commitment.	Clear accountability and definition of done
Medium	Add and verify schedule dates for CK-4 to CK-6.	More complete Gantt / roadmap evidence
Medium	Capture beginning, midpoint and end-of-sprint burndown views.	Meaningful progress comparison

Key lesson: Jira becomes useful evidence only when issue hierarchy, ownership, estimates, dates and status are kept complete and consistent. The supplied project demonstrates the core Agile workflow, while the evidence gaps show exactly what should be tightened for the next lab.


Evidence A - Jira timeline / Gantt-style view with sprint and epic scheduling

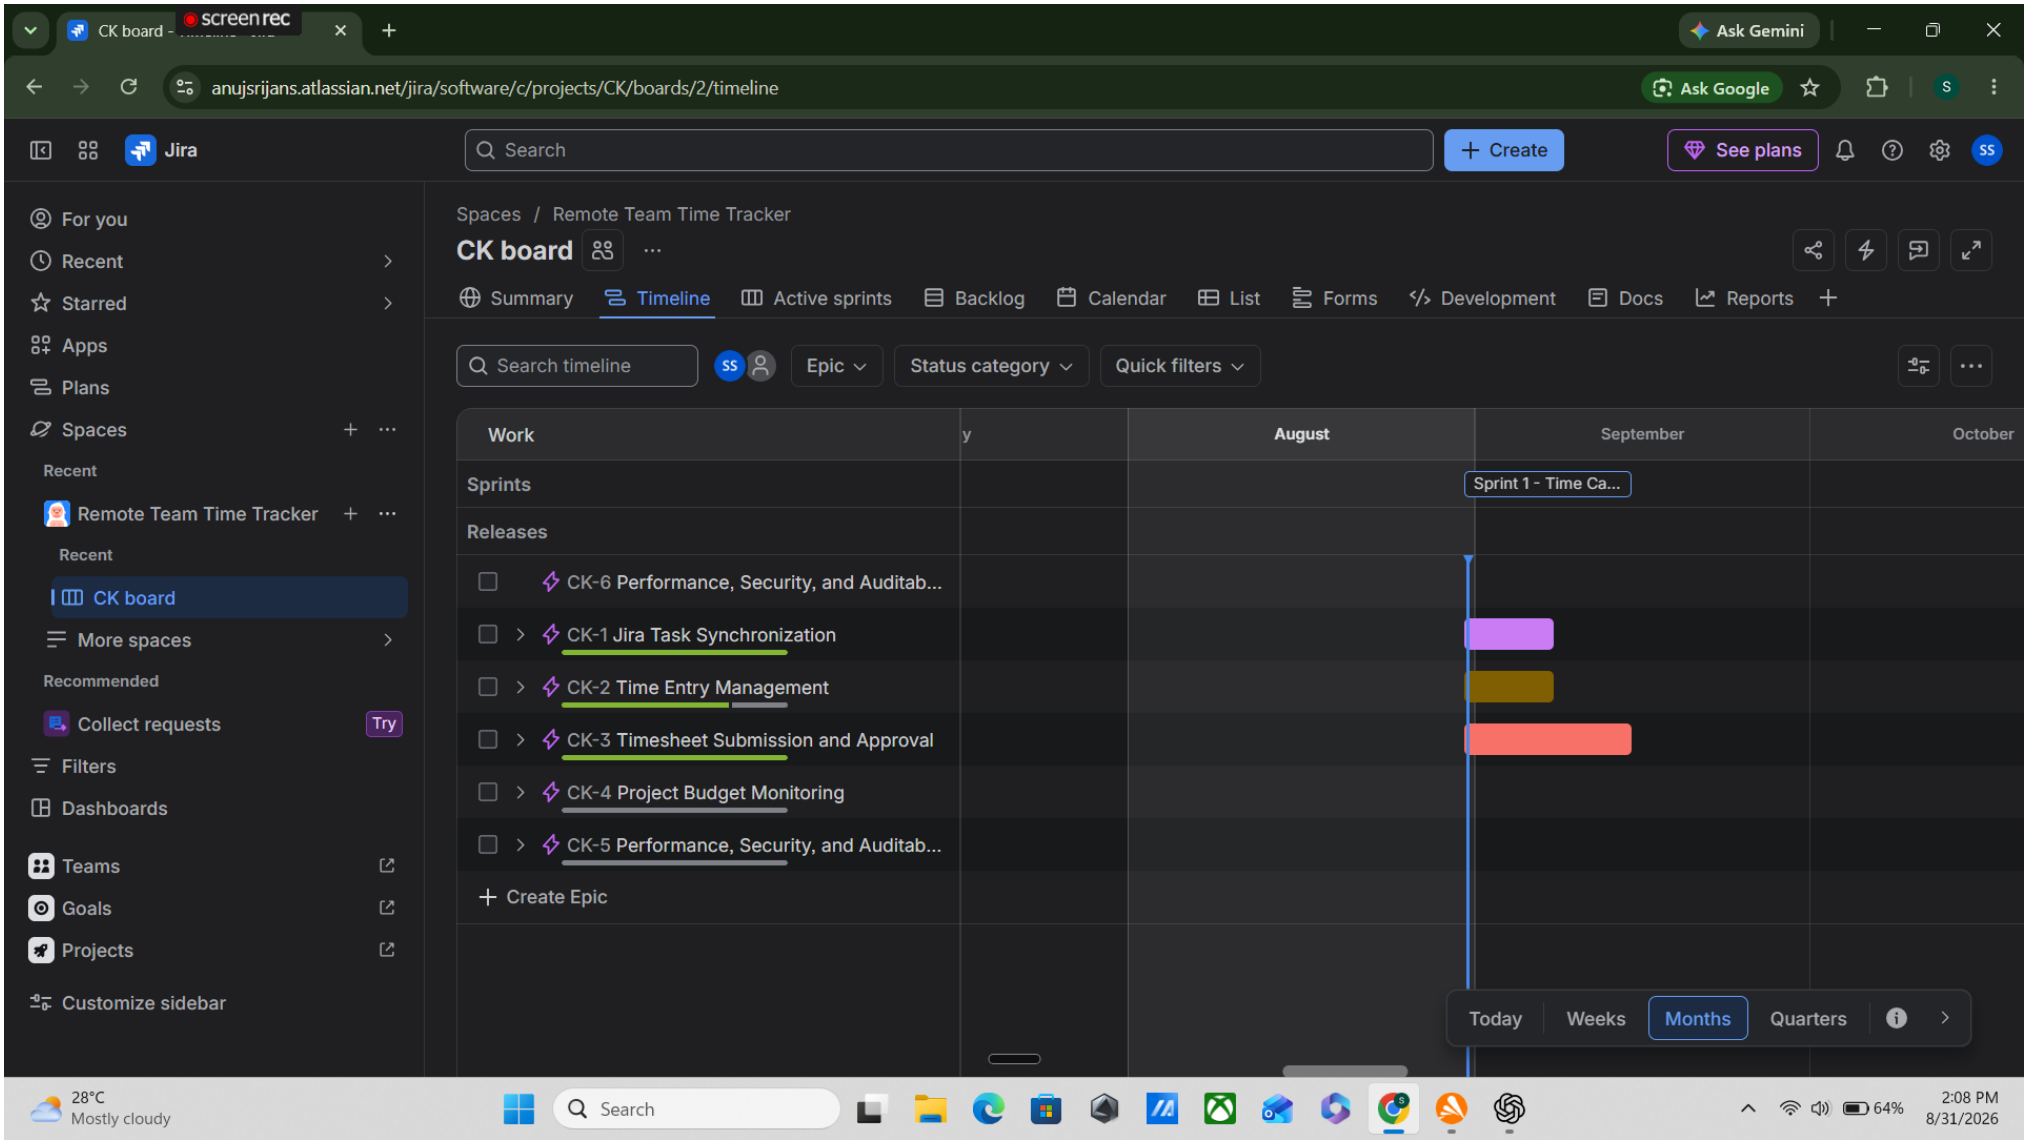


Evidence B - Backlog with epic panel, completed Sprint 1 and remaining stories

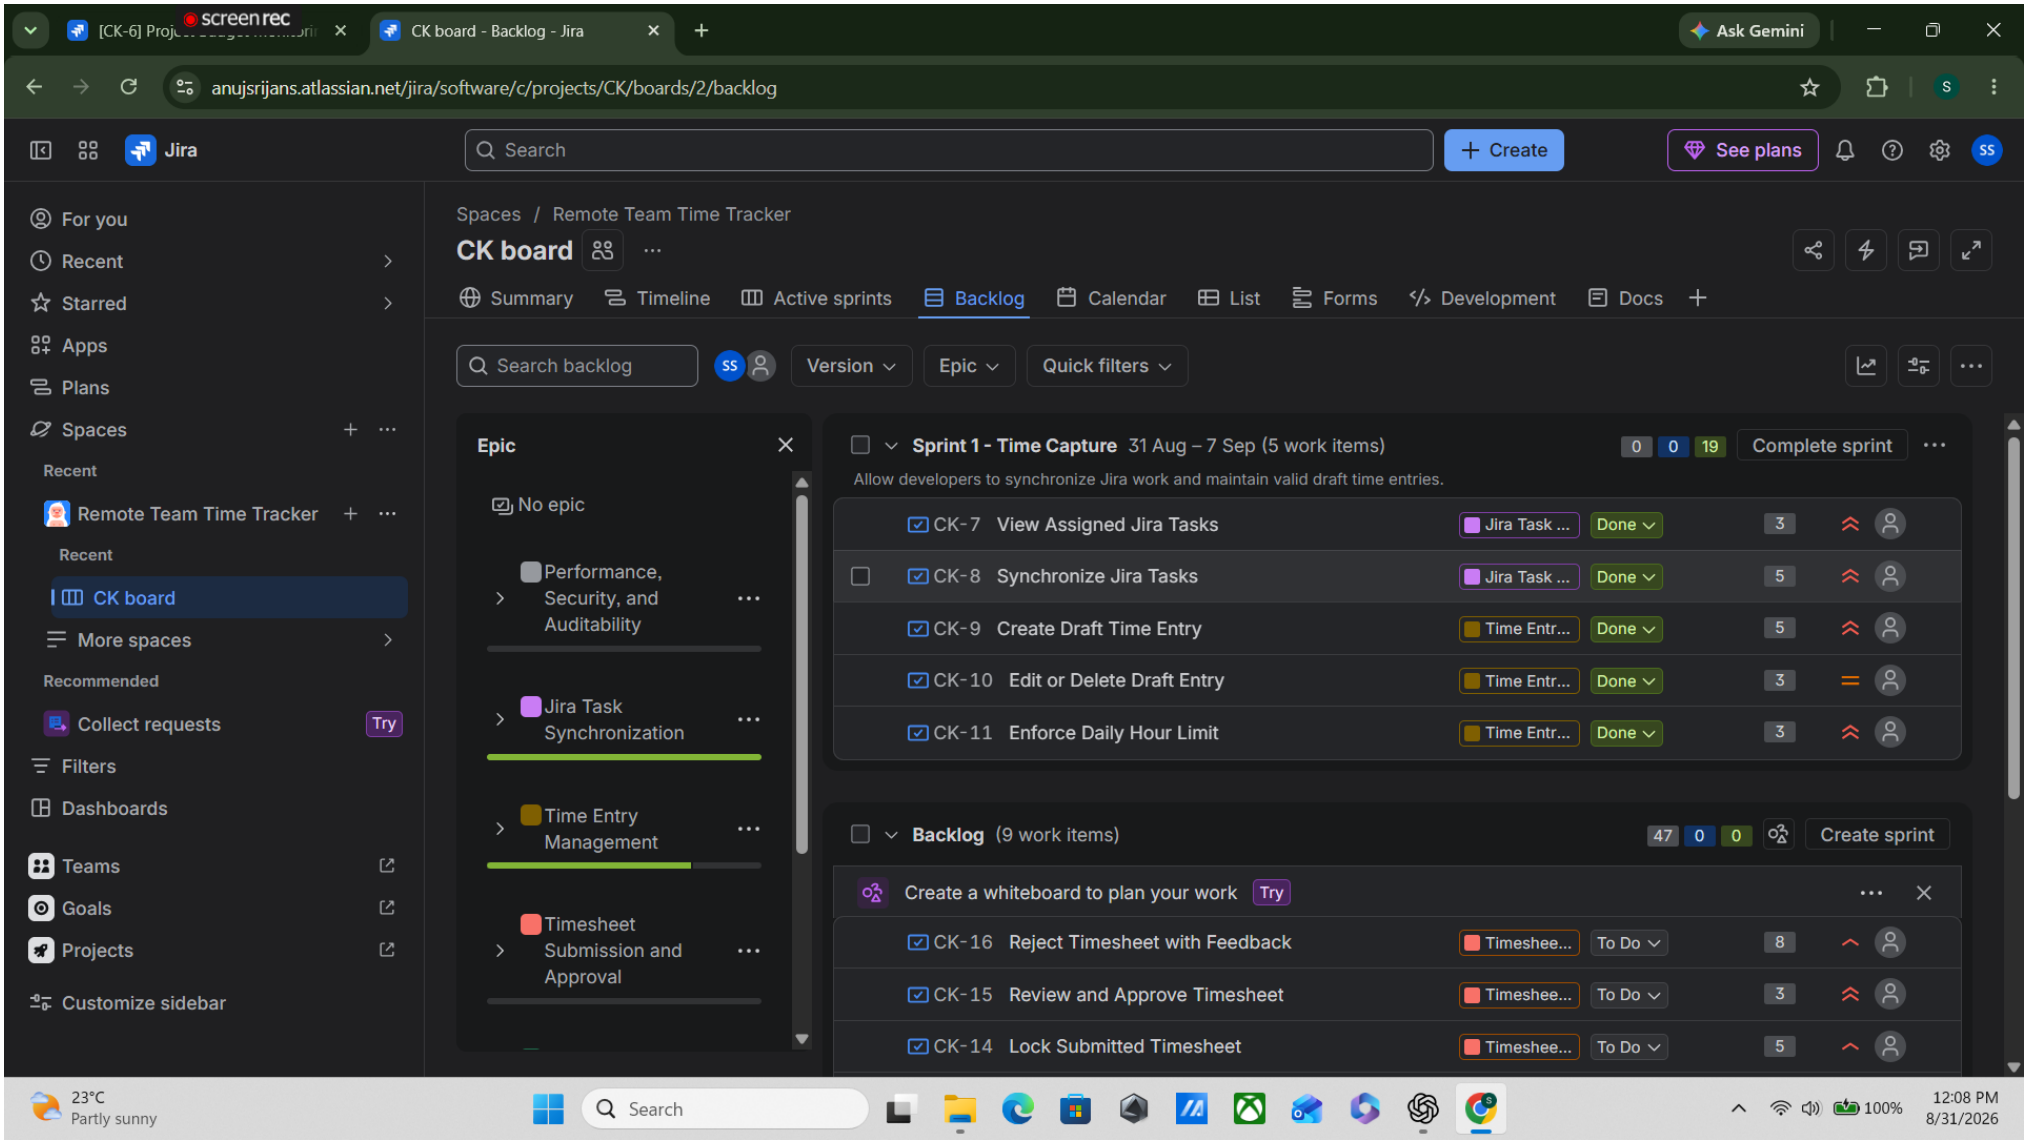


Evidence C - Expanded Sprint 1 story list with keys, points and Done status

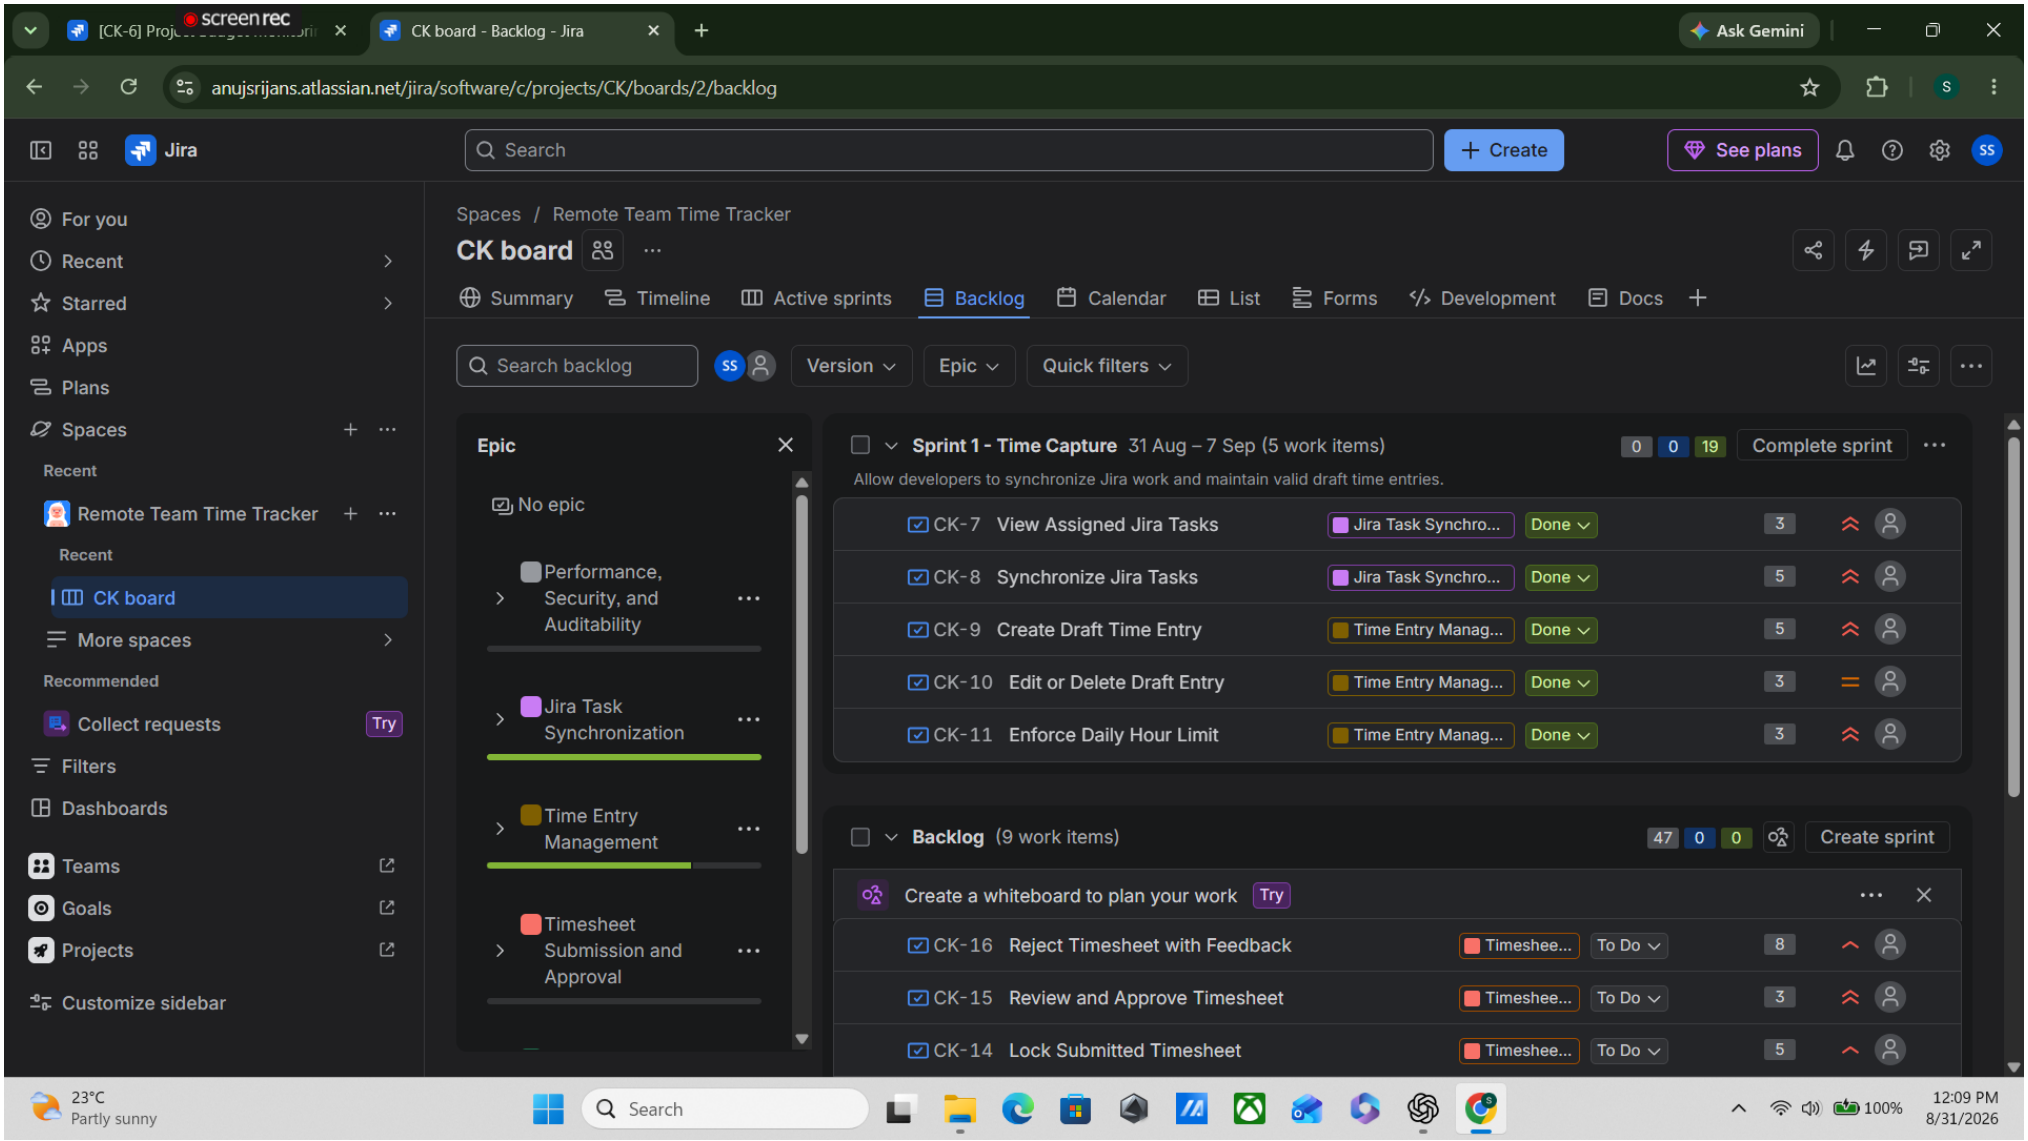


Evidence D - Active sprint board showing To Do, In Progress and Done columns

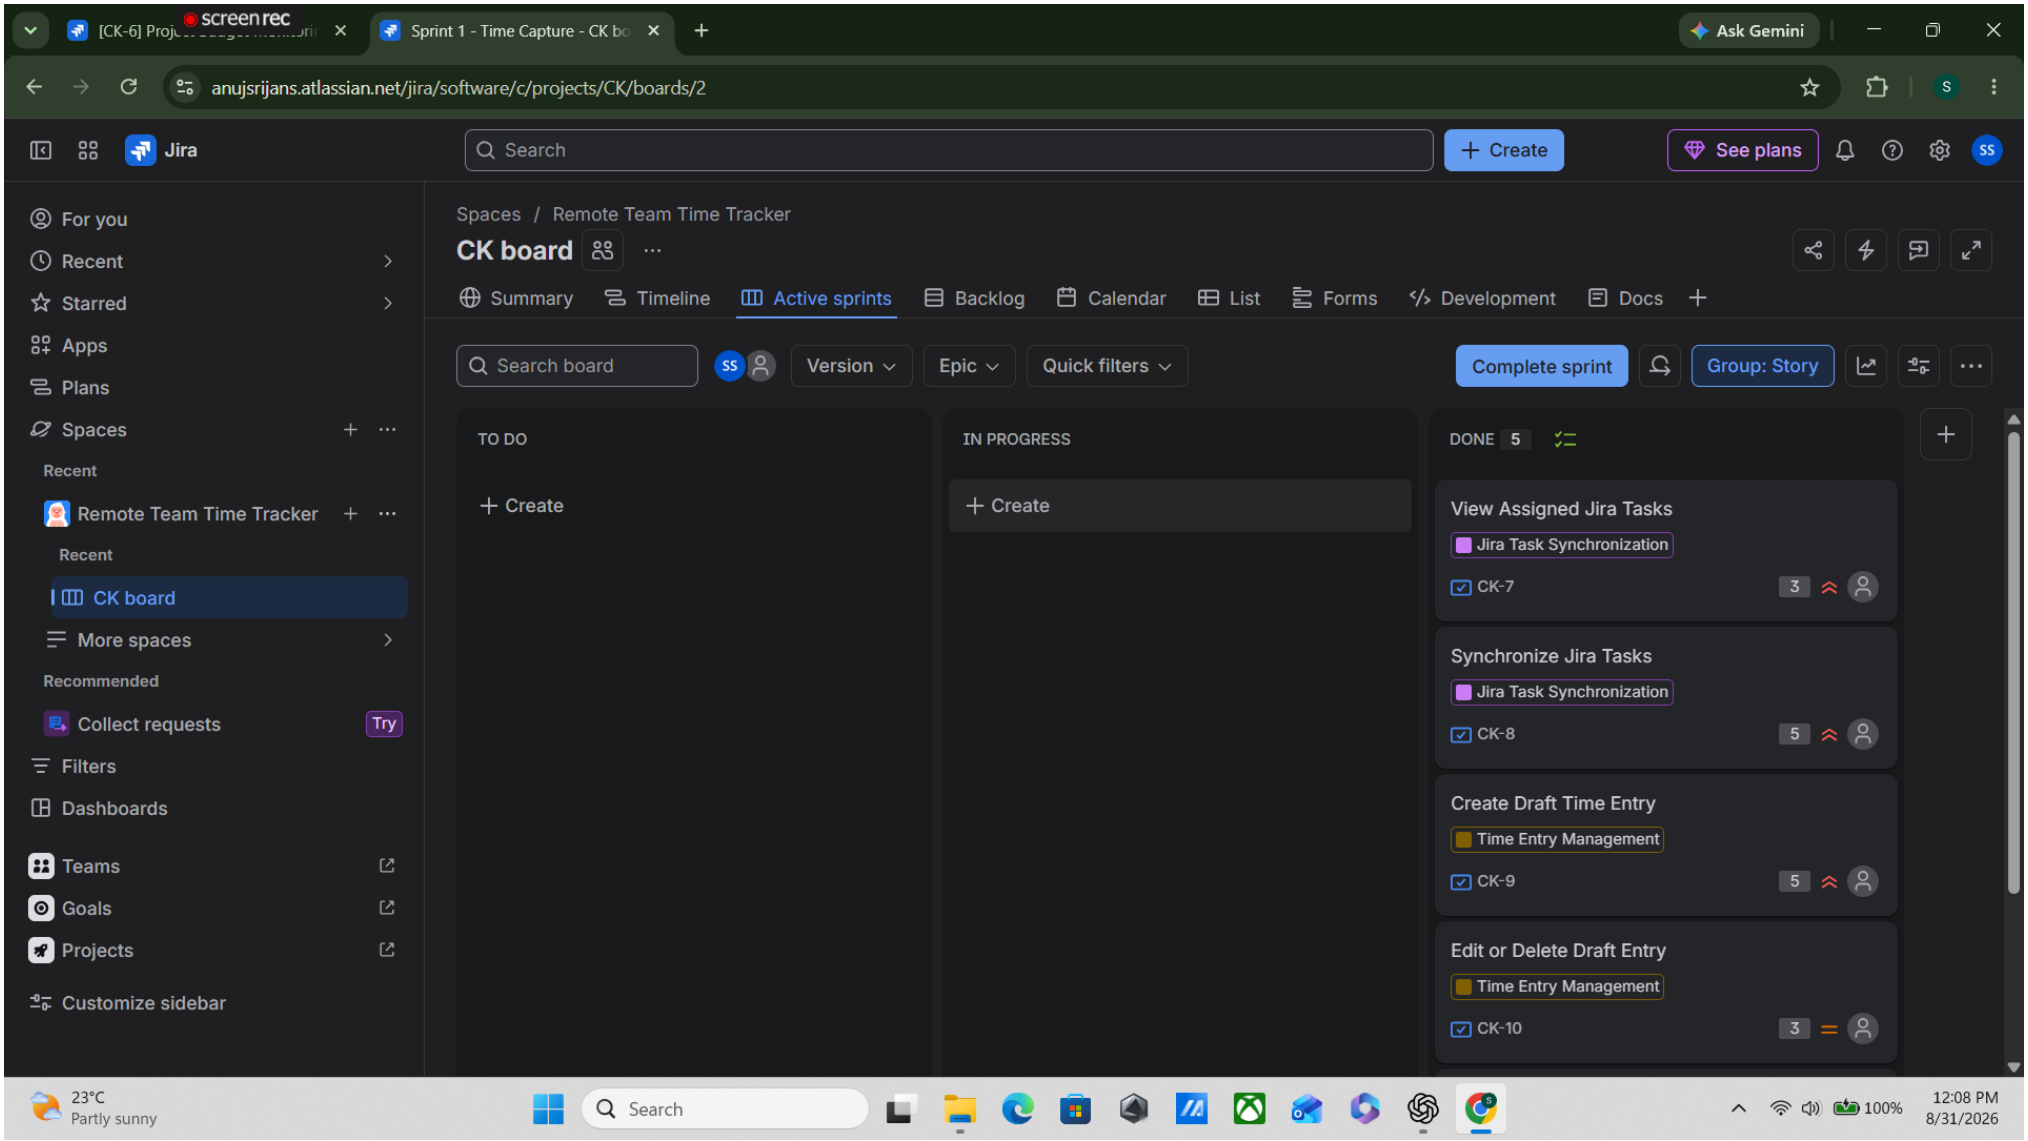


Evidence E - Final project summary: 9 completed and 11 To Do

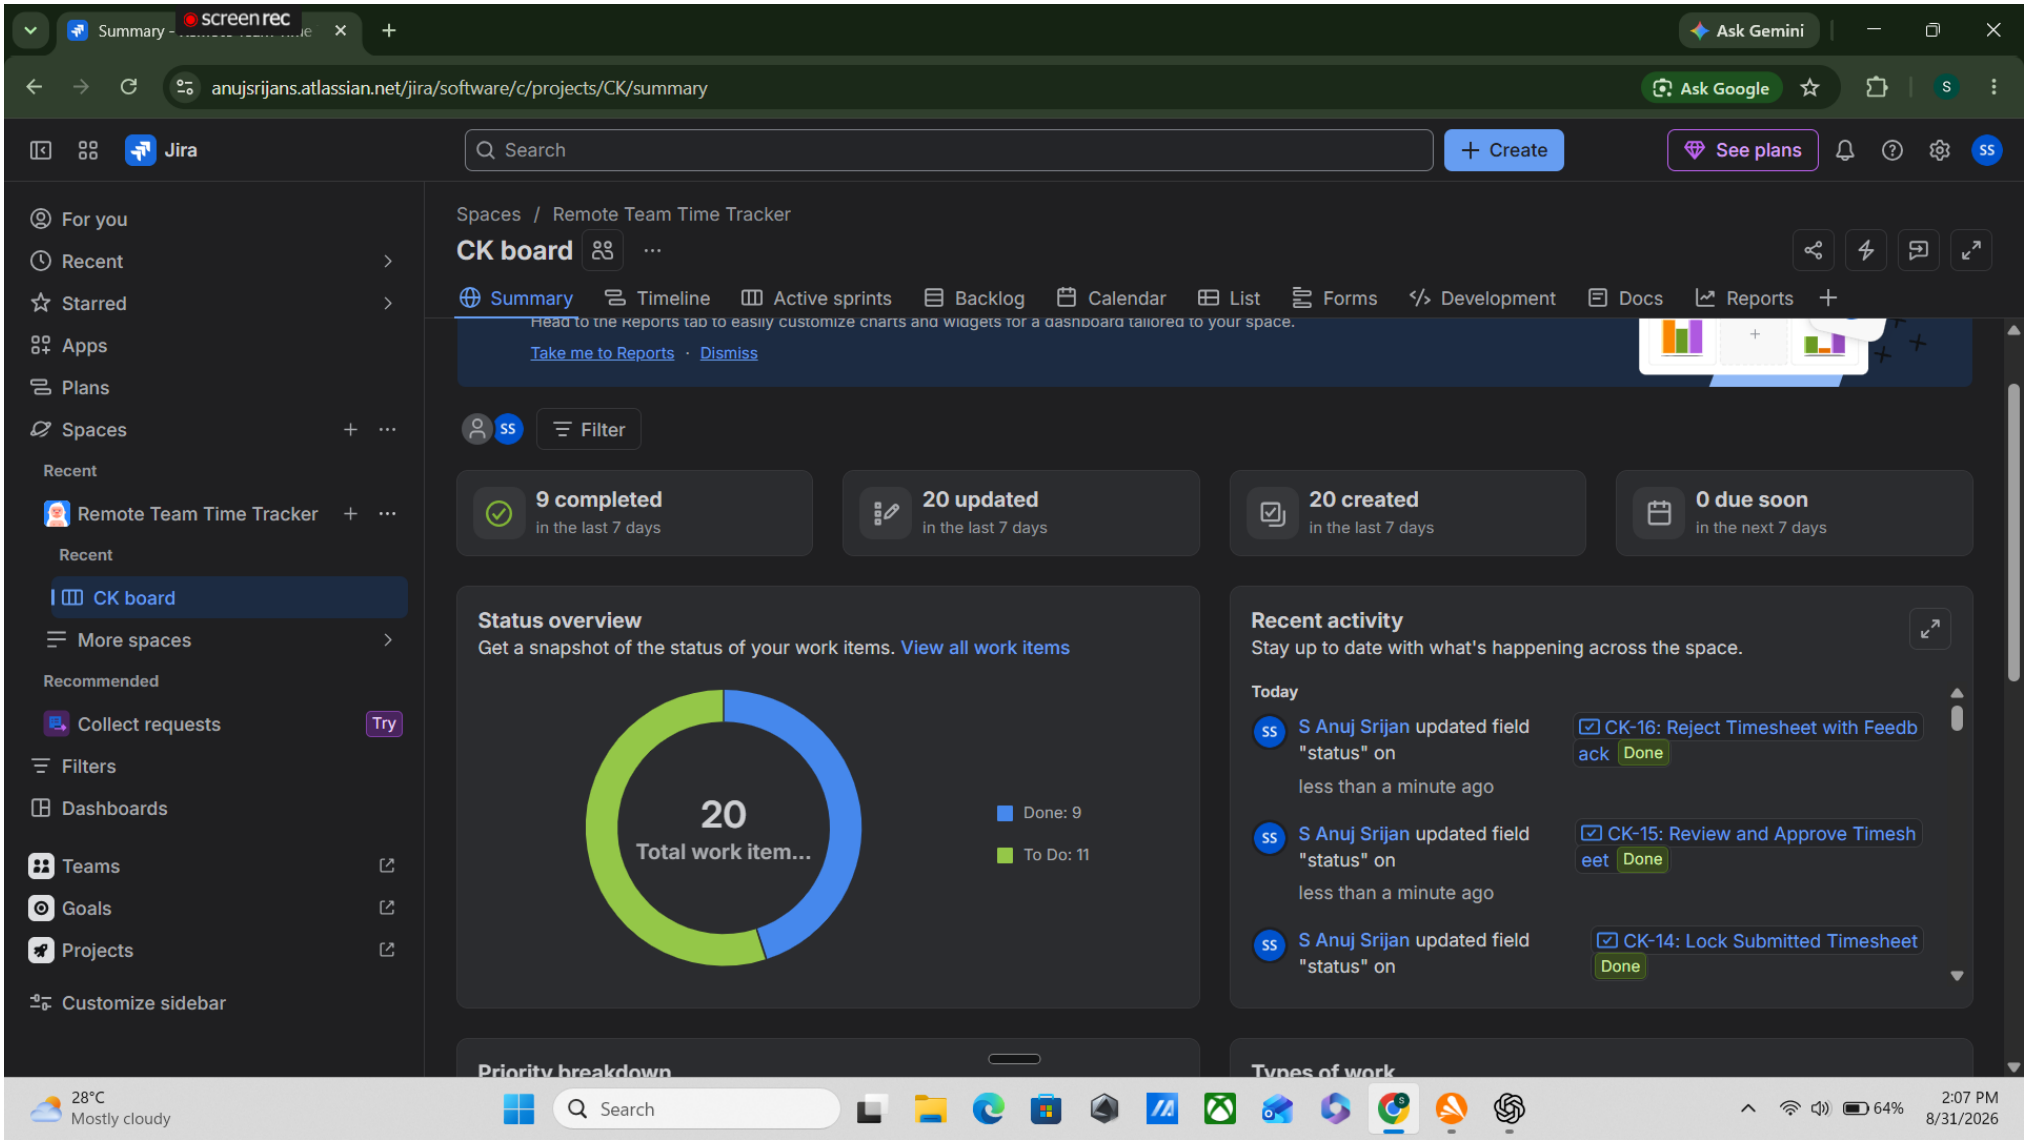


Evidence F - Earlier project summary: 5 completed and 15 To Do

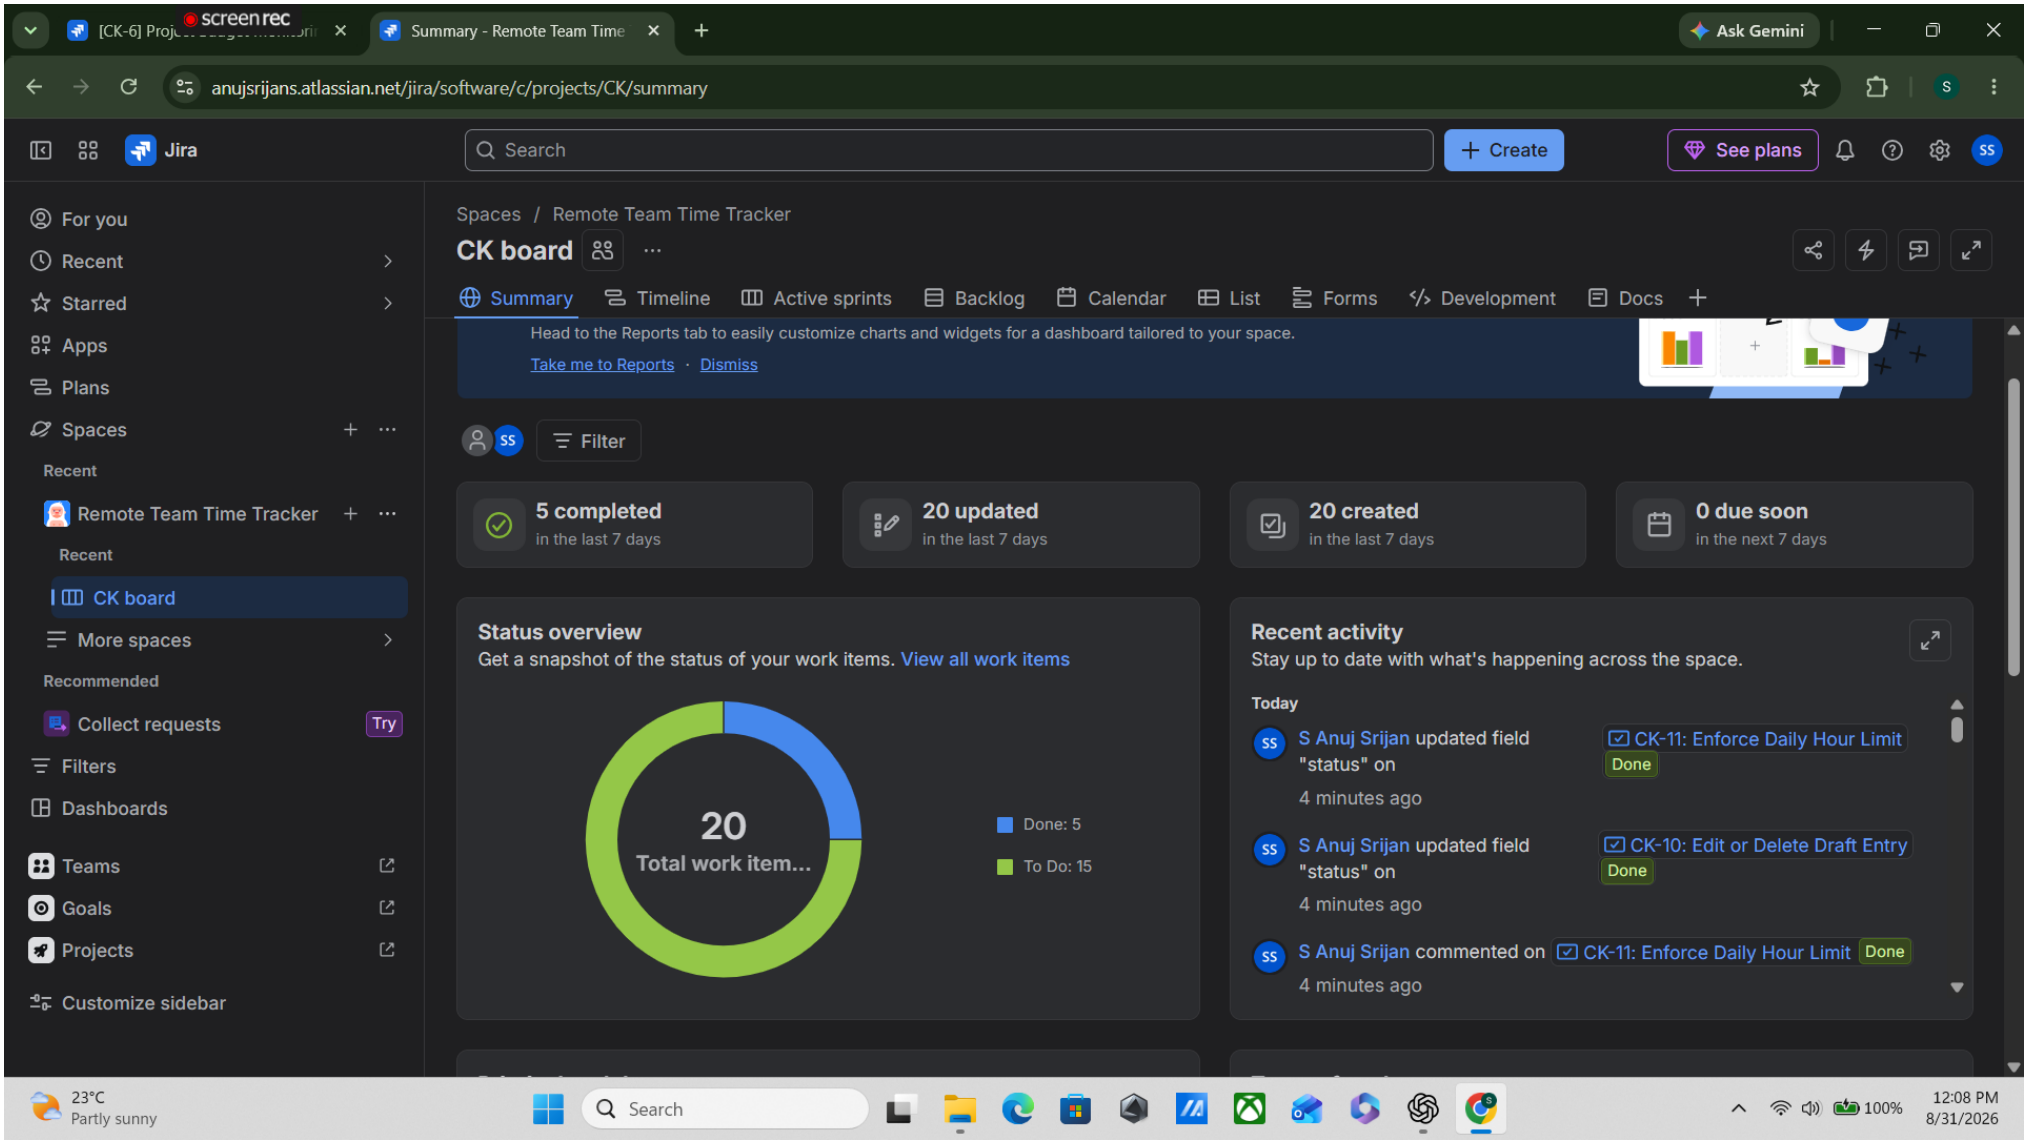


Evidence G - Jira reporting: work-item creation trend and cycle time

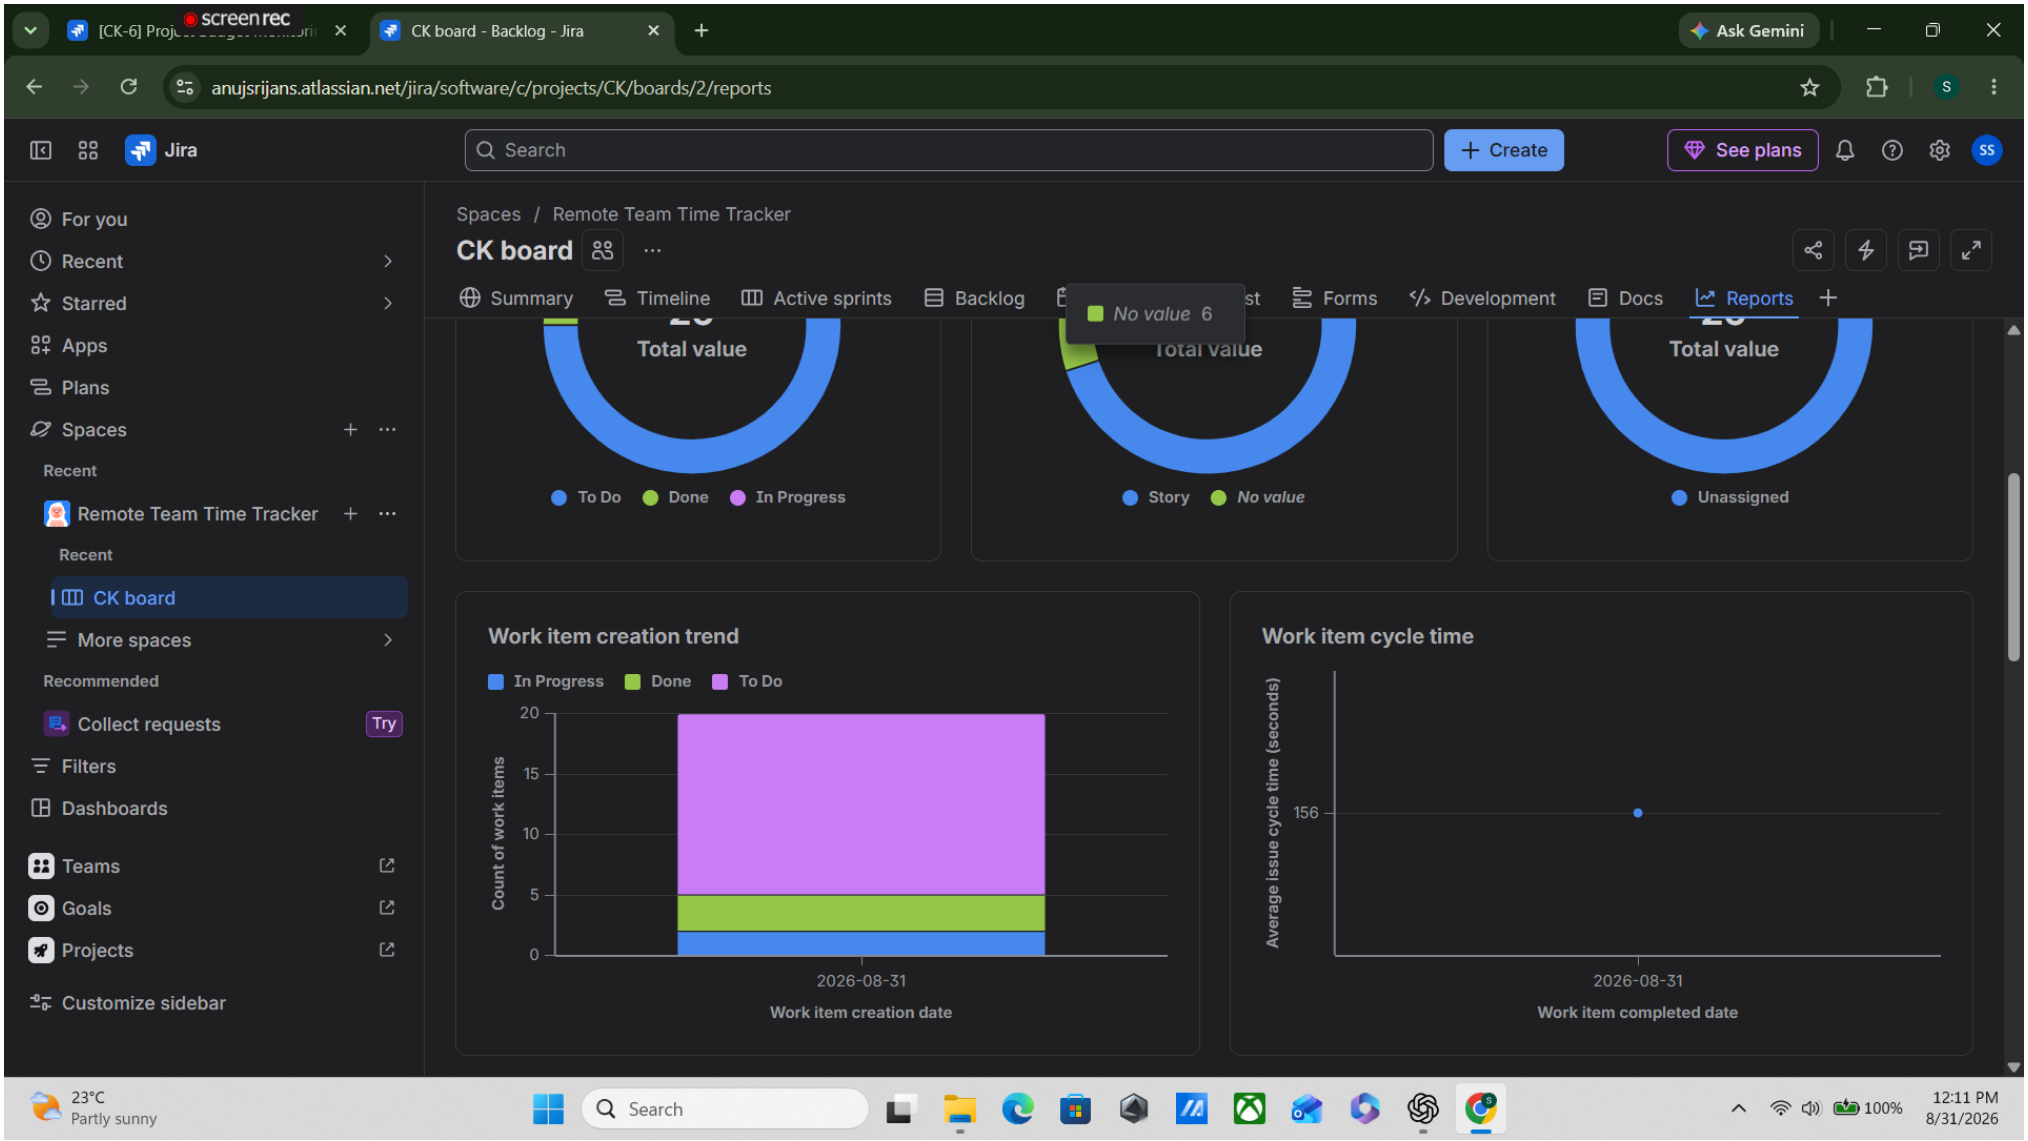


Evidence H - Sprint 1 burndown chart

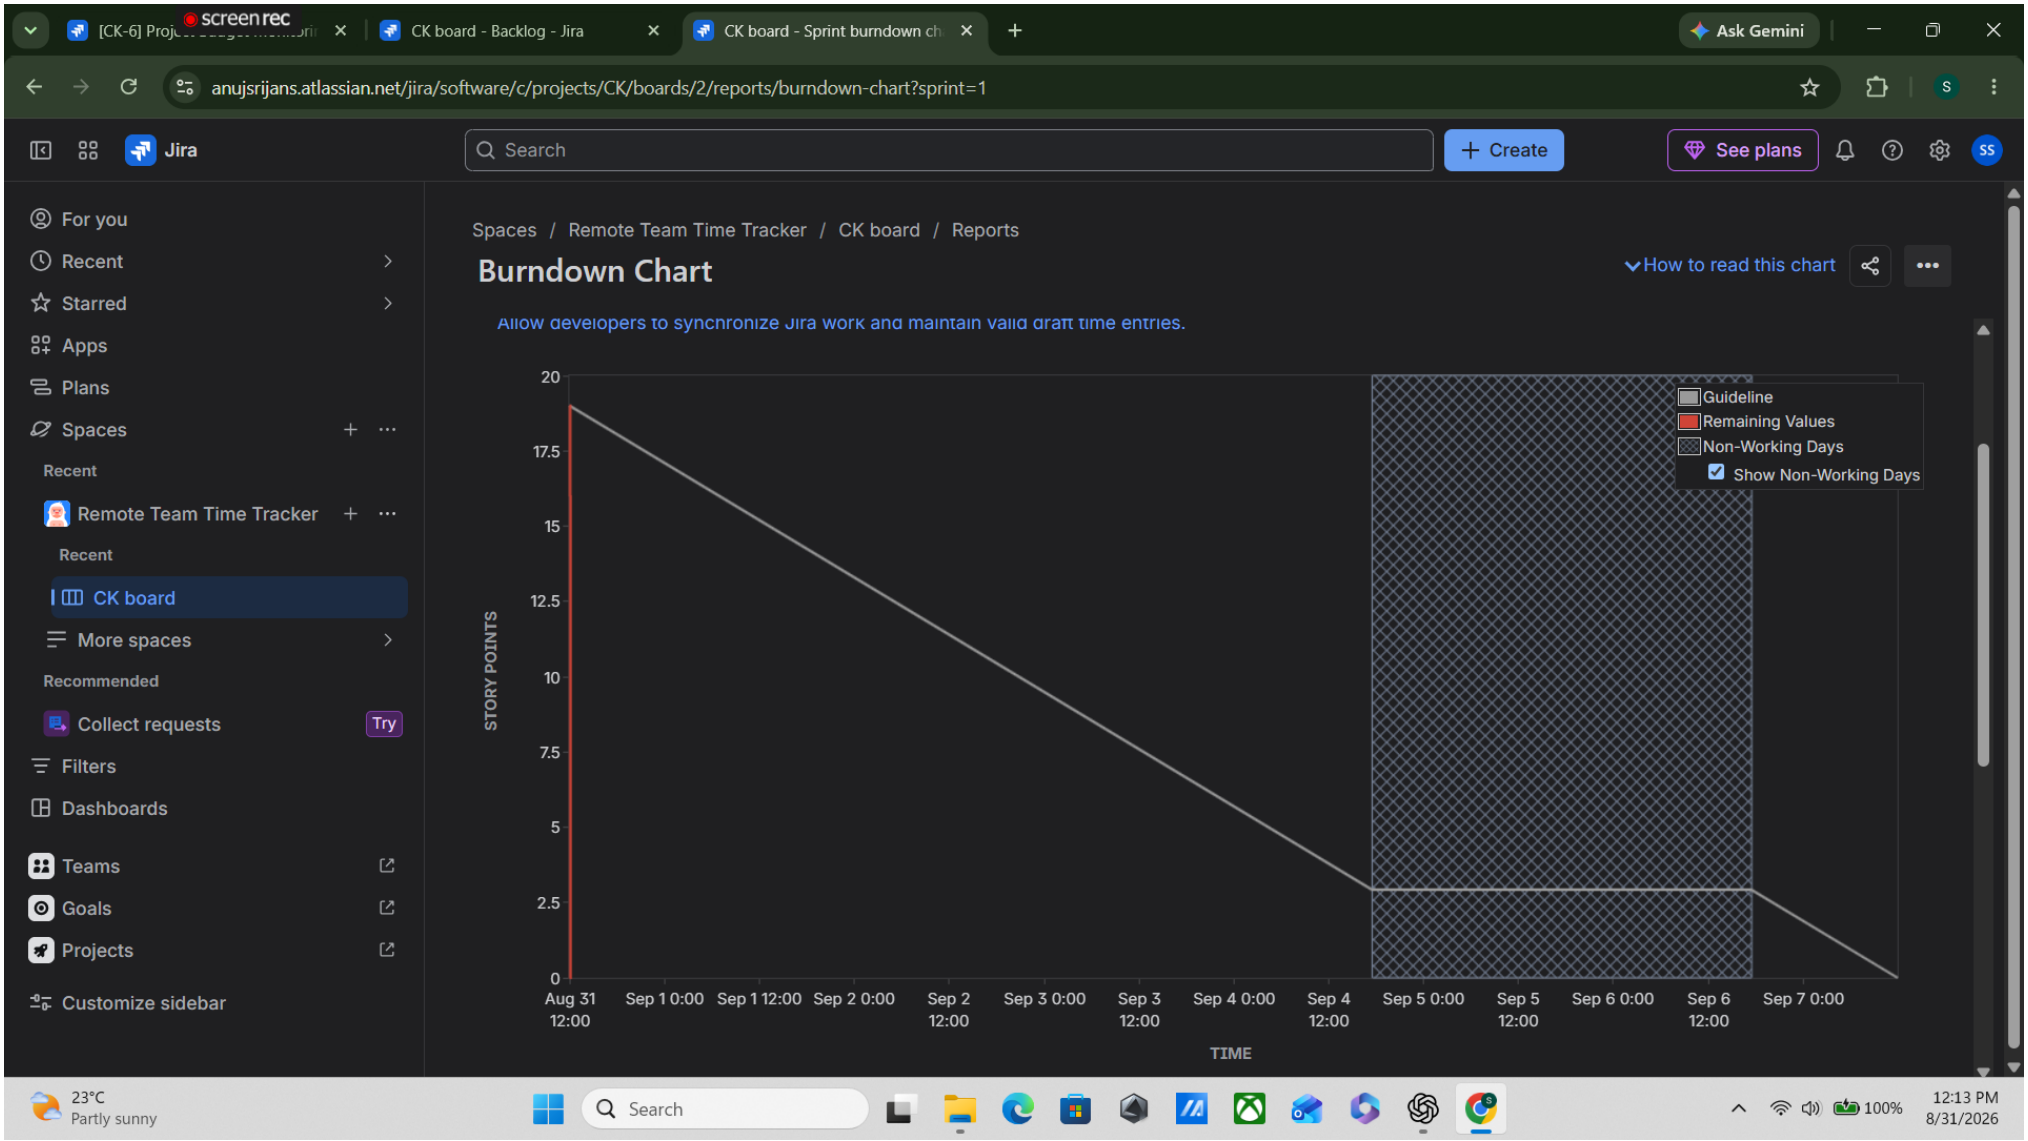

Evidence I - Sprint 2 burndown chart

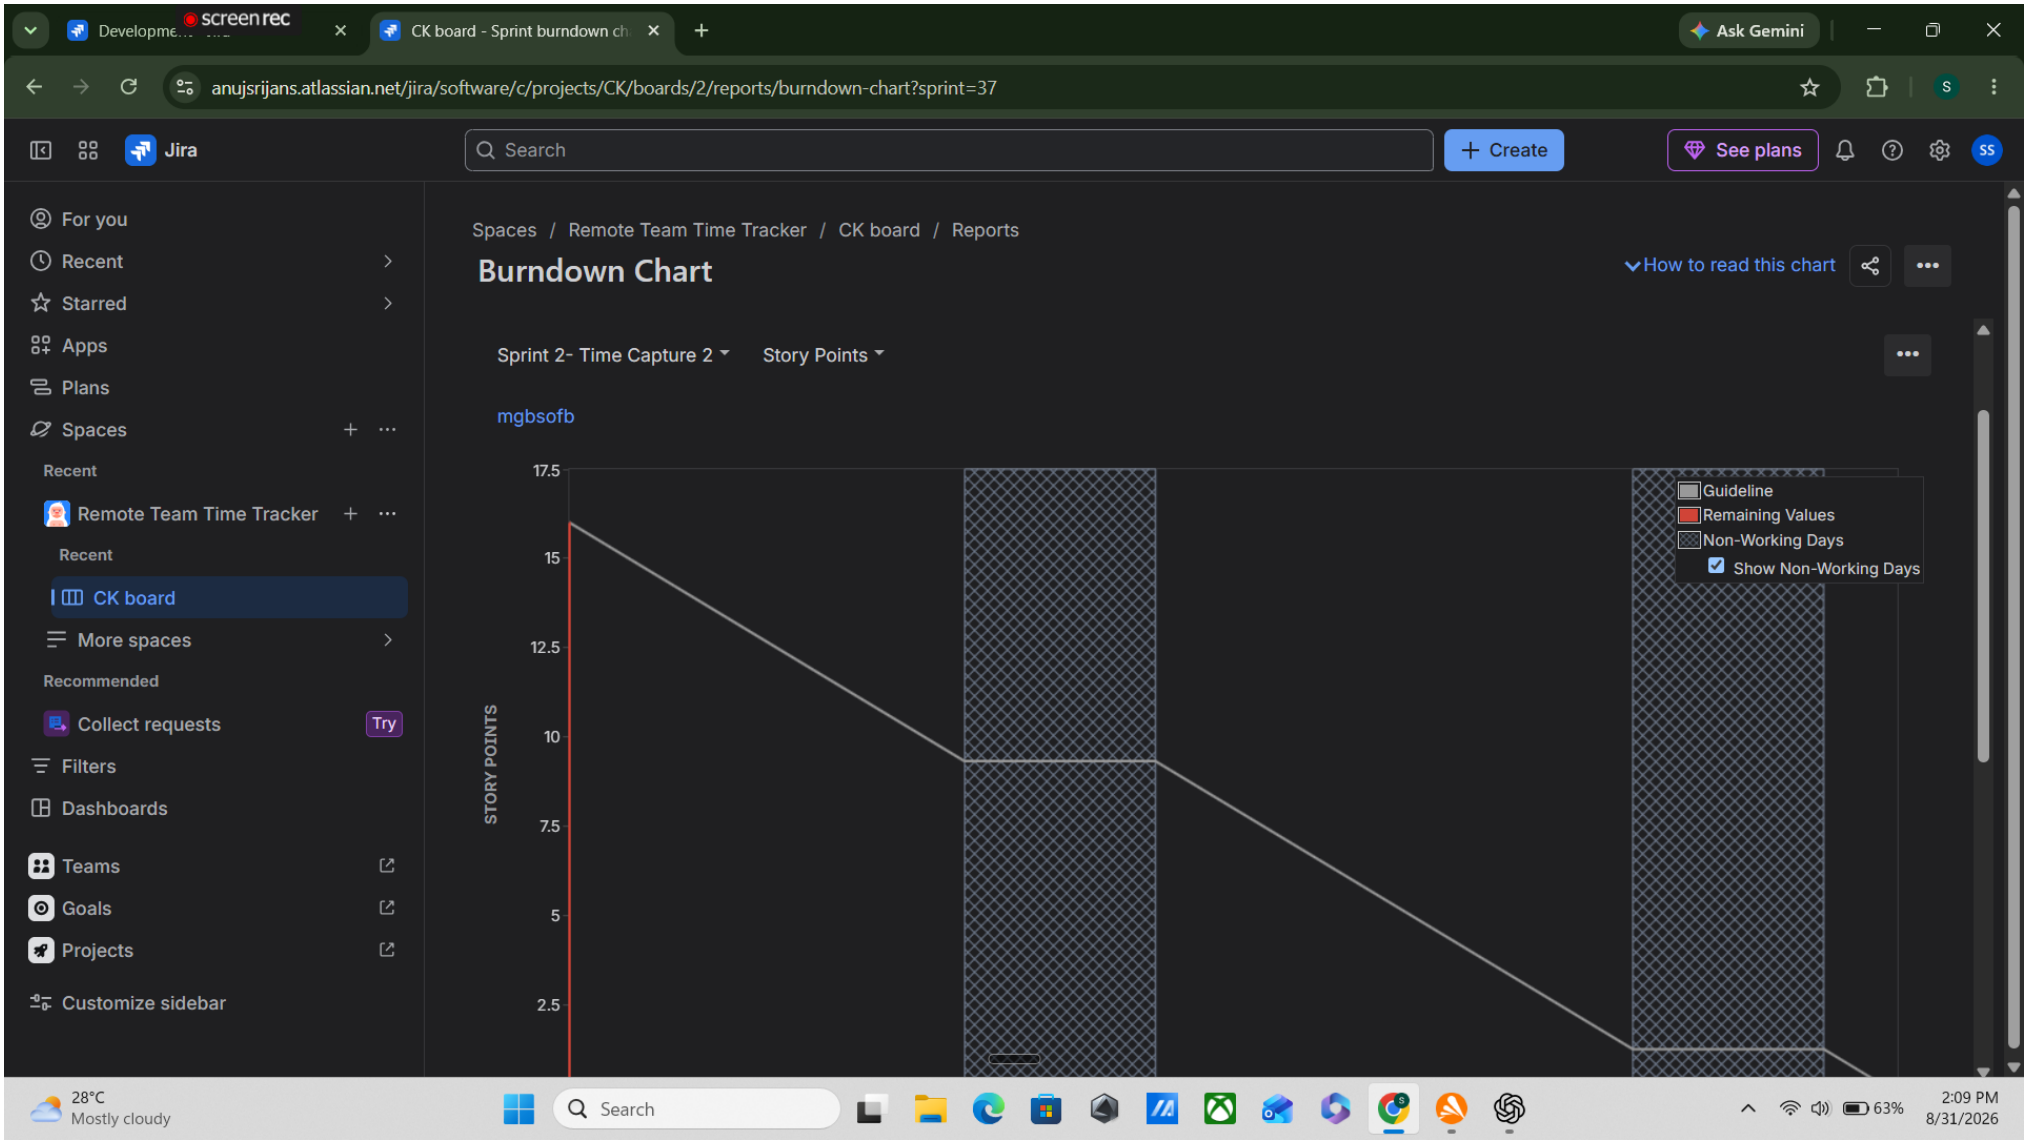

Evidence J - Sprint 2 completion dialog and remaining backlog

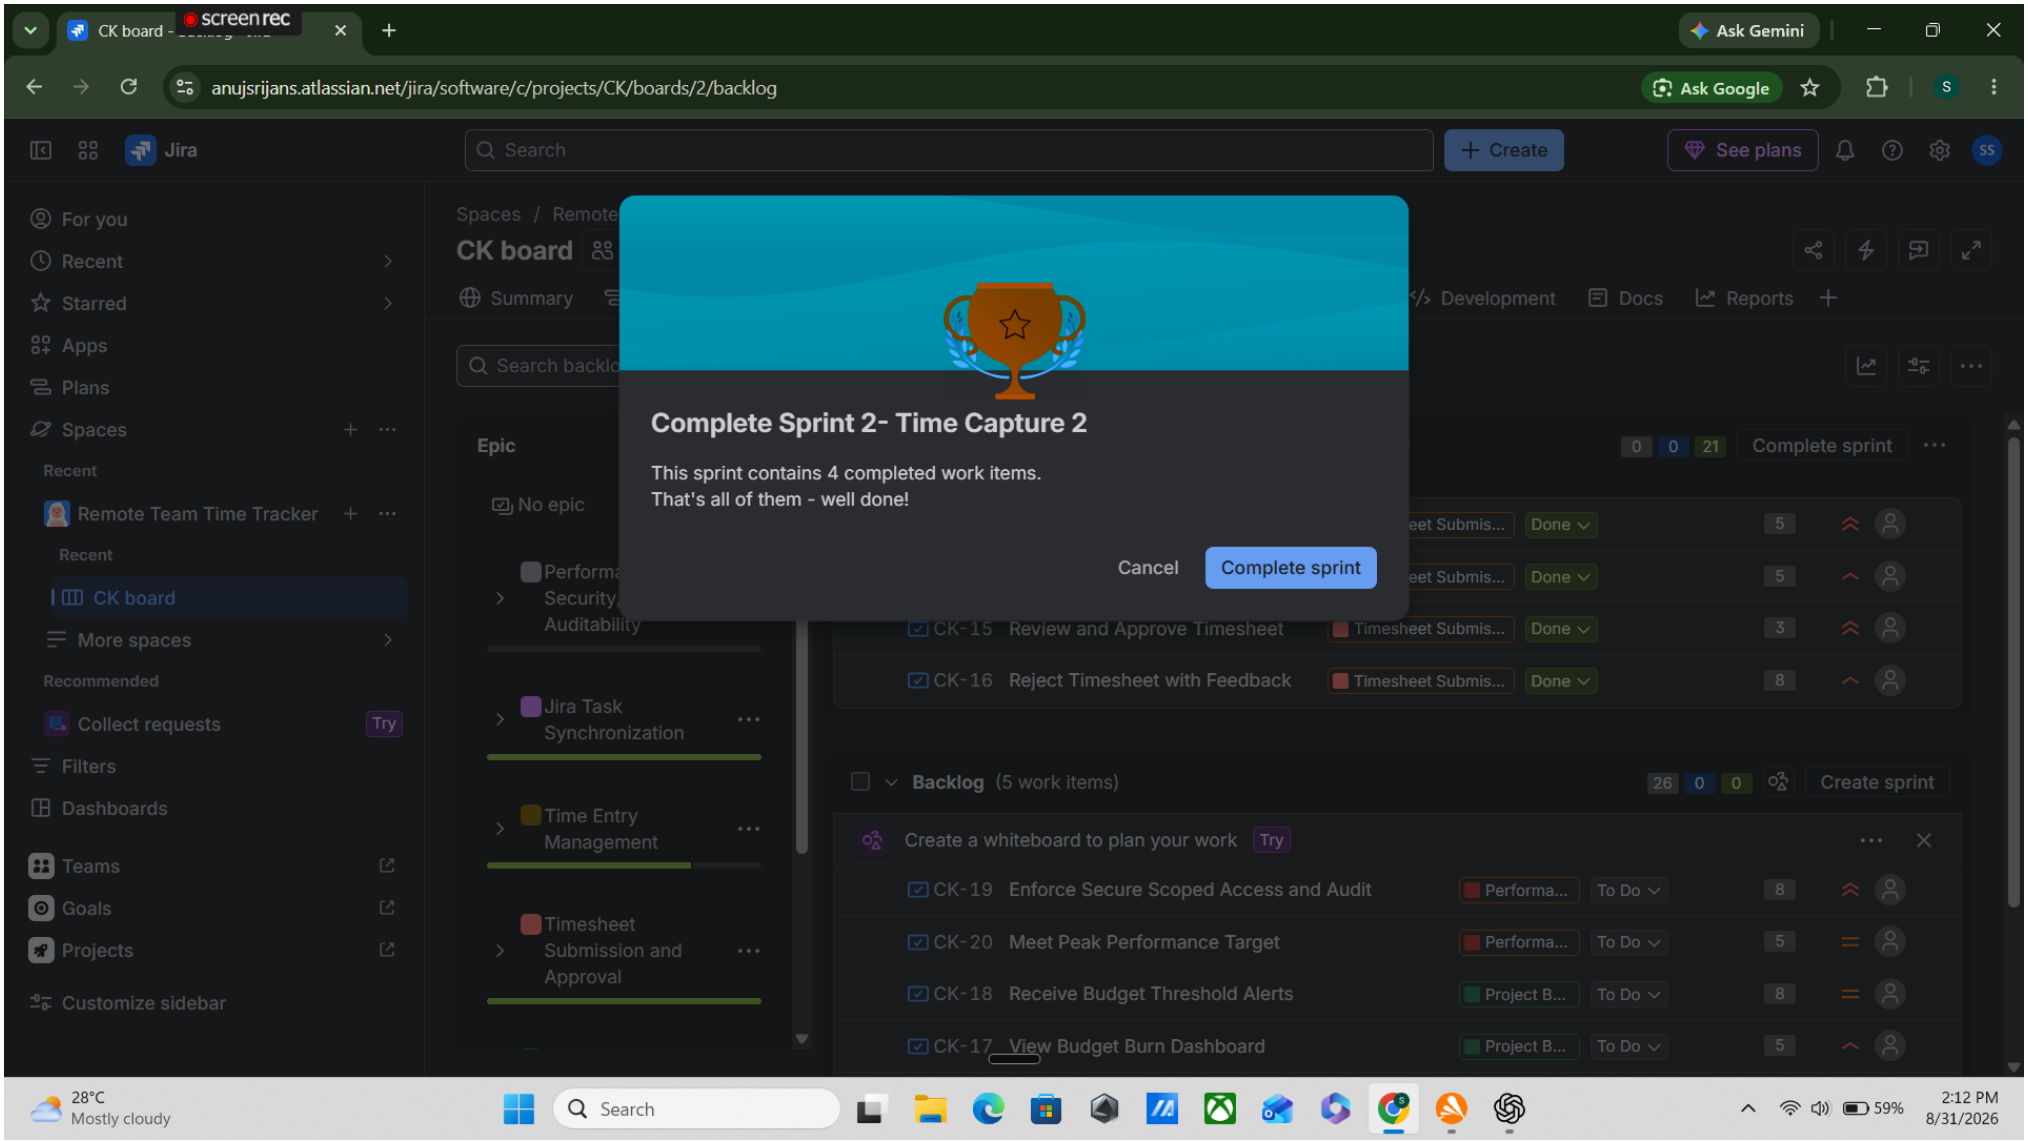

Evidence K - Initial timeline view and six-epic register

